


	Vol Flow Rate BEFORE INTERVENTION		Vol Flow Rate AFTER INTERVENTION
DP [Pa]		DP [Pa]	
6.5	594.7	8	637.1
10.5	926.0	11.5	849.5
15	1163.8	16	1056.8
20	1529.1	20	1214.8
26	1775.5	26.5	1495.1
29.5	1928.4	31.5	1656.5
35.5	2208.7	37	1834.9
41	2421.1	43	2021.8
40	2395.6	47	2174.7
46	2718.4	50.5	2276.7
51.5	2888.3	53	2344.6
59.5	3143.2	61	2548.5
60	3143.2		
	Before		After
@50Pa	<b>2832.4</b>		<b>2257.1</b>



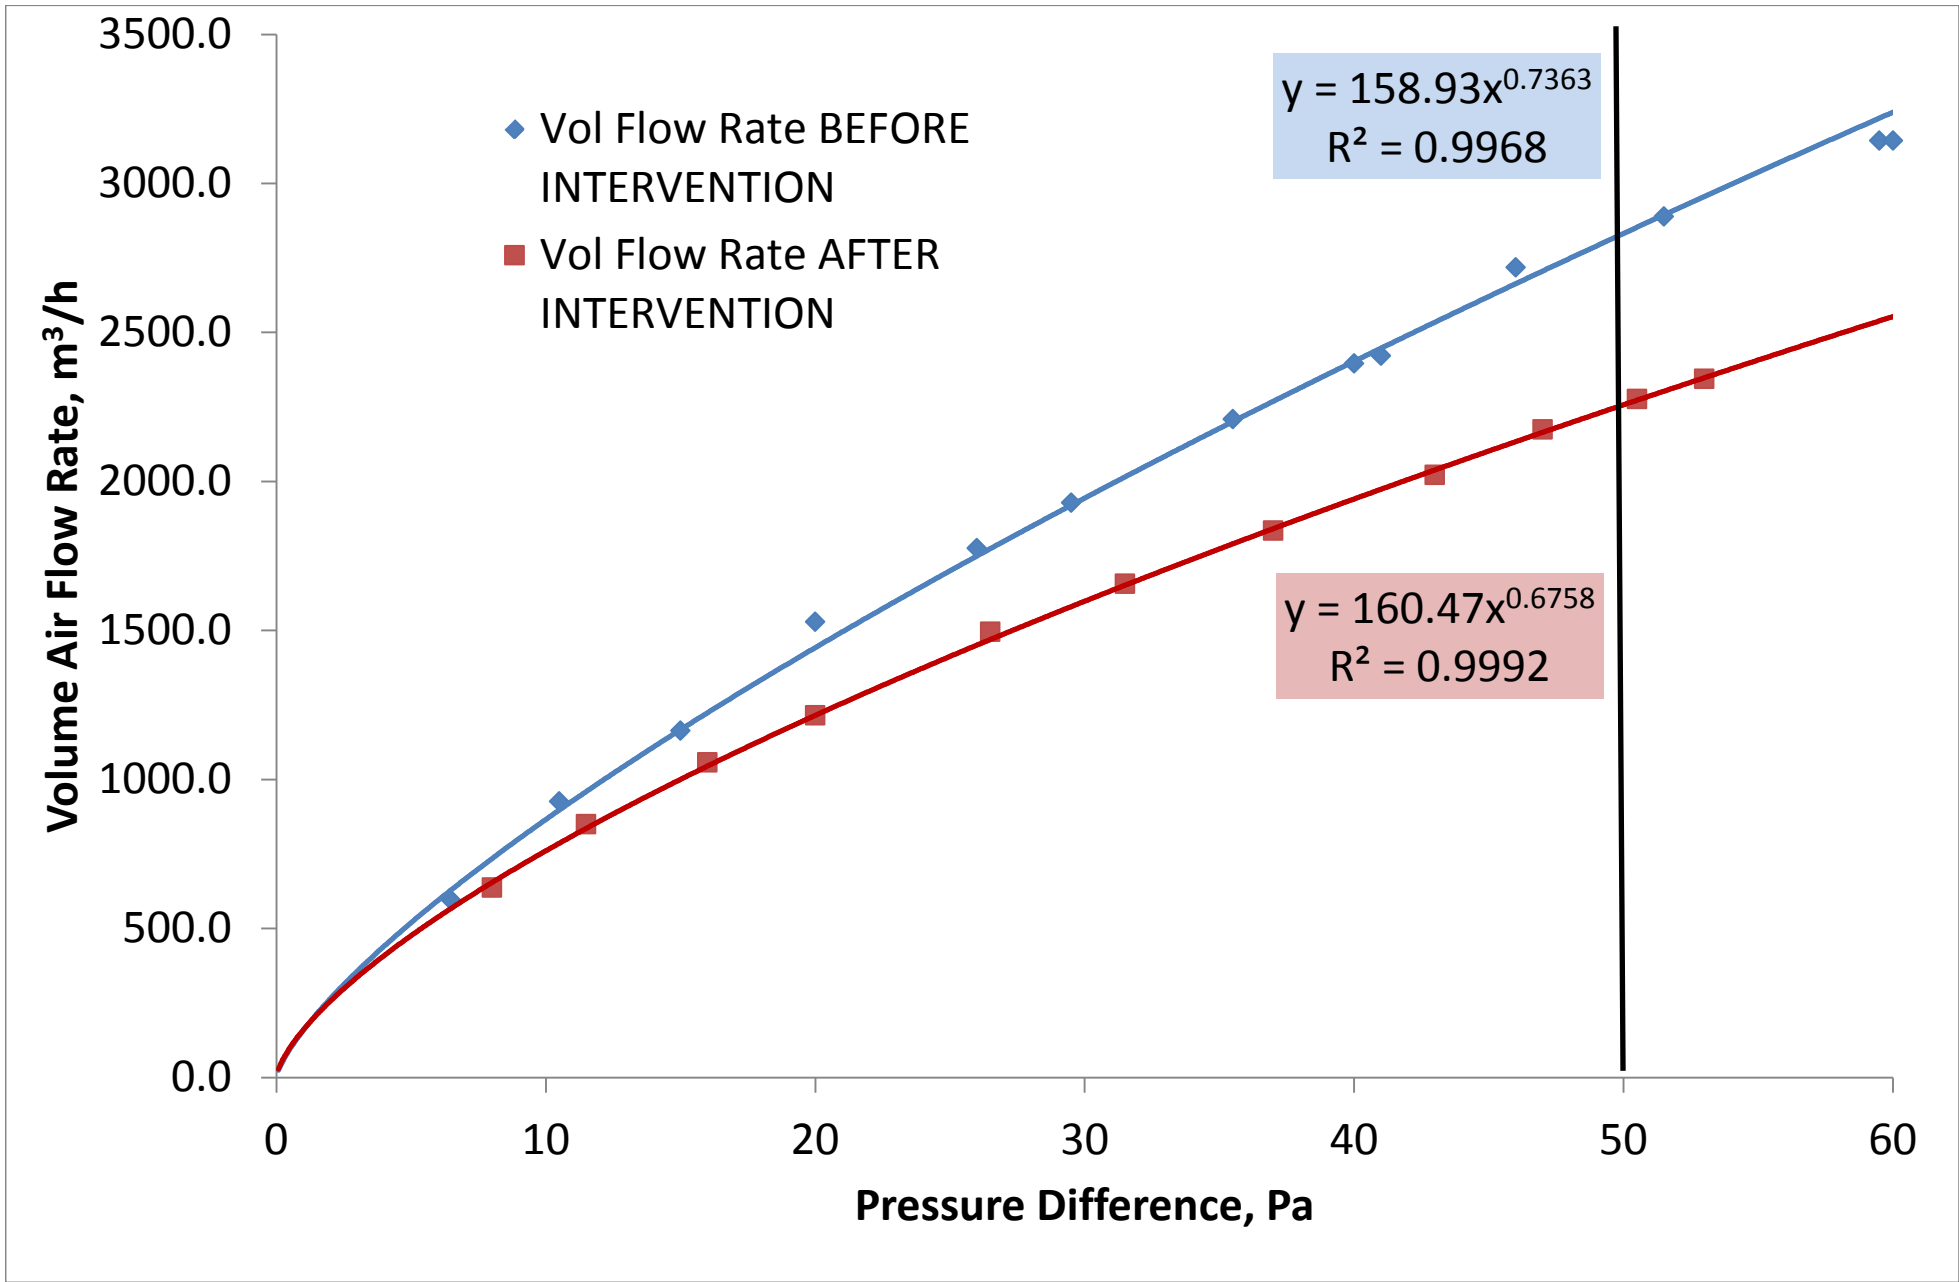

	AREA m <sup>2</sup>	VOL m <sup>3</sup>	m <sup>3</sup> /h @ 50Pa	ACH @ 50Pa	Envelope Air leakage Index m <sup>3</sup> /h per m <sup>2</sup> envelope area @ 50Pa
Before Intervention June 2011	226.2	219.1	2832.4	12.9	<b>12.5</b>
After Intervention March 2012	218.4	209.6	2257.1	10.8	<b>10.3</b>
